

PROJECT PLANNING PHASE

Project Planning Template (Product Backlog, Sprint Planning, Stories, Story points)

Date	
Team ID	
Project Name	Auto-Ticket Classification using Flow Designer
Maximum Marks	5 Marks

Product Backlog, Sprint Schedule, and Estimation

The planning structure follows the supplied reference: a sprint is a fixed work period, an epic is a larger work area, a story is a smaller task within an epic, and story points use the 1, 2, 3 and 5 scale. The backlog below organizes the twelve documented project work items across five sprints.

Sprint	Functional Requirement (Epic)	Story No.	User Story / Task	Points	Priority	Assignee
Sprint-1	Requirement Analysis & Planning	US-01	Define school IT helpdesk problem, business requirement & target workflow.	2	High	Aditya A
Sprint-1	Requirement Analysis & Planning	US-02	Create Project Update Set to track table, form and flow customizations.	3	High	Aditya A
Sprint-2	Backend Dev & Schema Config	US-03	Create School IT Ticket custom table and School IT Support module.	5	High	Akash N A
Sprint-2	Backend Dev & Schema Config	US-04	Create fields for number, caller, category, subcategory, state, assignment.	3	High	Akash N A
Sprint-2	Backend Dev & Schema Config	US-05	Configure Category choices and make Subcategory dependent on Category.	3	High	Akash N A
Sprint-3	Flow Designer Automation	US-06	Create Auto Classify School IT Tickets flow with Record Created trigger.	5	High	Radha K P
Sprint-3	Flow Designer Automation	US-07	Implement conditions for Wi-Fi, Projector, Password, Performance.	3	High	Radha K P
Sprint-3	Flow Designer Automation	US-08	Send acknowledgment email to Caller after ticket creation.	3	Medium	Radha K P
Sprint-4	Testing & Validation	US-09	Test automatic classification by creating ticket with supported description.	3	High	Ferdin Joe A
Sprint-4	Testing & Validation	US-10	Verify email notification and validate resulting ticket records.	2	High	Ferdin Joe A
Sprint-5	Deployment & Packaging	US-11	Complete Project Update Set and review captured customer updates.	3	High	Simeon P
Sprint-5	Deployment & Packaging	US-12	Export Update Set to XML for repository storage and deployment.	2	High	Simeon P

Sprint Story Point Summary

Sprint	Epic / Milestone	Team Member	Story Points
Sprint-1	Requirement Analysis & Planning	Aditya A	5
Sprint-2	Backend Development & Schema Configuration	Akash N A	11
Sprint-3	Flow Designer Automation	Radha Krishnan P	11
Sprint-4	Testing & Validation	Ferdin Joe A	5
Sprint-5	Deployment & Packaging	Simeon P	5
Total	All five milestones	Project Team	37

The 37-point total is a planning estimate mapped to the twelve documented work items. It is not presented as a historical point total from the SkillWallet board.

Project Tracker, Velocity & Burndown Chart

Sprint	Total Story Points	Duration	Sprint Start Date	Sprint End Date (Planned)	Story Points Completed	Sprint Release Date (Actual)
Sprint-1	5	1 Day	28 September 2026	28 September 2026	5	28 September 2026
Sprint-2	11	1 Day	29 September 2026	29 September 2026	11	29 September 2026
Sprint-3	11	1 Day	30 September 2026	30 September 2026	11	30 September 2026
Sprint-4	5	1 Day	01 October 2026	01 October 2026	5	01 October 2026
Sprint-5	5	1 Day	01 October 2026	01 October 2026	5	01 October 2026

Velocity

Total planned story points = 37. Number of planned sprints = 5.
Average velocity = Total Story Points / Number of Sprints = 37 / 5 = **7.4 story points per sprint**.

Agile Sprint Delivery Workflow




Figure 1: Agile sprint execution lifecycle across five milestones.

Burndown Chart

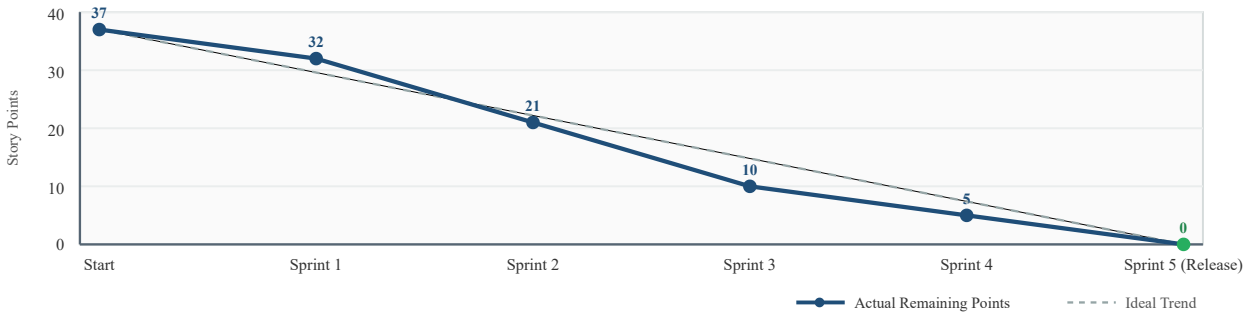


Figure 2: Planned project burndown based on estimated 37 story points.

Burndown Chart Explanation: The burndown chart tracks remaining story points across five sprints. The project begins with 37 points. Following Sprint 1, 32 points remain; Sprint 2 completes 11 points (21 remaining); Sprint 3 completes 11 points (10 remaining); Sprint 4 completes 5 points (5 remaining); and Sprint 5 completes the final 5 points, achieving 0 remaining effort at deployment.

Implementation Evidence

The following screenshots connect the planned stories with the actual ServiceNow implementation.

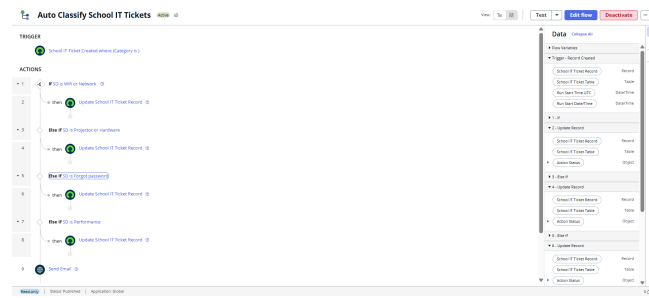


Figure 3: Published Auto Classify School IT Tickets Flow Designer workflow.

The screenshot shows the 'School IT Tickets' list in ServiceNow. The table contains the following data:

Number	Assigned Group	Assigned to	Caller	Category	Description	Short description	Subcategory
19710001010	Internal	jdoe	Internal	System Administrator	WS off morning in library	WS off morning in library	
19710001011	Internal	jdoe	Internal	System Administrator	Prognosis not working on	Prognosis not working on	
19710001012	Internal	jdoe	Internal	System Administrator	WS off morning in library	WS off morning in library	
19710001013	Internal	jdoe	Internal	Network	WS off morning in library	WS off morning in library	

Figure 4: School IT Tickets list showing created records and classification results.

Implementation Evidence - Testing and Deployment

The screenshot shows the 'School IT Ticket' form in ServiceNow. The form is titled 'School IT Ticket - TKT000012'. It has a 'Name' field with the value 'TKT000012'. The 'Description' field contains 'Web 2.0 web marketing library'. The 'Category' is set to 'Network' and the 'Subcategory' is set to 'Web 2.0'. The 'Status' is set to 'None'. The 'Assigned Group' and 'Assigned To' fields are empty. The 'Update' and 'Cancel' buttons are visible at the bottom.

Figure 5: School IT Ticket showing automatic Category and Subcategory classification.

The screenshot shows the 'Project Update Set' form in ServiceNow. The form is titled 'Project Update Set'. It has a 'Name' field with the value 'Project Update Set'. The 'Status' is set to 'Complete'. The 'Release Date' is set to '2020-09-28 12:15:17'. The 'Created By' is 'ADMIN'. The 'Updated By' is 'ADMIN'. The 'Updated On' is '2020-09-28 12:15:17'. The 'Description' field is empty. Below the form, there is a table with the following data:

Customer	Customer ID	Update Set Name	Update Set Type	Update Set Status	Update Set Description	Update Set Created By	Update Set Created On	Update Set Updated By	Update Set Updated On	Update Set Action
School IT Support	2020-09-28 12:15:17	School IT Support	Project Update Set	Complete		ADMIN	2020-09-28 12:15:17	ADMIN	2020-09-28 12:15:17	Import
School IT Tickets	2020-09-28 12:15:17	School IT Tickets	Project Update Set	Complete		ADMIN	2020-09-28 12:15:17	ADMIN	2020-09-28 12:15:17	Import
School IT Ticket Category	2020-09-28 12:15:17	School IT Ticket Category	Project Update Set	Complete		ADMIN	2020-09-28 12:15:17	ADMIN	2020-09-28 12:15:17	Import
School IT Ticket Subcategory	2020-09-28 12:15:17	School IT Ticket Subcategory	Project Update Set	Complete		ADMIN	2020-09-28 12:15:17	ADMIN	2020-09-28 12:15:17	Import
School IT Ticket	2020-09-28 12:15:17	School IT Ticket	Project Update Set	Complete		ADMIN	2020-09-28 12:15:17	ADMIN	2020-09-28 12:15:17	Import
School IT Ticket Assigned Group	2020-09-28 12:15:17	School IT Ticket Assigned Group	Project Update Set	Complete		ADMIN	2020-09-28 12:15:17	ADMIN	2020-09-28 12:15:17	Import

Figure 6: Completed Project Update Set with captured customer updates and the Export to XML option.
