

PROJECT PLANNING PHASE

Project Planning Template (Product Backlog, Sprint Planning, Stories, Story points)

Date	
Team ID	
Project Name	Auto-Ticket Classification using Flow Designer
Maximum Marks	5 Marks

Product Backlog, Sprint Schedule, and Estimation

The planning structure follows the supplied reference: a sprint is a fixed work period, an epic is a larger work area, a story is a smaller task within an epic, and story points use the 1, 2, 3 and 5 scale. The backlog below organizes the twelve documented project work items across five sprints.

Sprint	Functional Requirement (Epic)	Story No.	User Story / Task	Points	Priority	Assignee
Sprint-1	Requirement Analysis & Planning	US-01	Define school IT helpdesk problem, business requirement & target workflow.	2	High	Aditya A
Sprint-1	Requirement Analysis & Planning	US-02	Create Project Update Set to track table, form and flow customizations.	3	High	Aditya A
Sprint-2	Backend Dev & Schema Config	US-03	Create School IT Ticket custom table and School IT Support module.	5	High	Akash N A
Sprint-2	Backend Dev & Schema Config	US-04	Create fields for number, caller, category, subcategory, state, assignment.	3	High	Akash N A
Sprint-2	Backend Dev & Schema Config	US-05	Configure Category choices and make Subcategory dependent on Category.	3	High	Akash N A
Sprint-3	Flow Designer Automation	US-06	Create Auto Classify School IT Tickets flow with Record Created trigger.	5	High	Radha K P
Sprint-3	Flow Designer Automation	US-07	Implement conditions for Wi-Fi, Projector, Password, Performance.	3	High	Radha K P
Sprint-3	Flow Designer Automation	US-08	Send acknowledgment email to Caller after ticket creation.	3	Medium	Radha K P
Sprint-4	Testing & Validation	US-09	Test automatic classification by creating ticket with supported description.	3	High	Ferdin Joe A
Sprint-4	Testing & Validation	US-10	Verify email notification and validate resulting ticket records.	2	High	Ferdin Joe A
Sprint-5	Deployment & Packaging	US-11	Complete Project Update Set and review captured customer updates.	3	High	Simeon P
Sprint-5	Deployment & Packaging	US-12	Export Update Set to XML for repository storage and deployment.	2	High	Simeon P

Sprint Story Point Summary

Sprint	Epic / Milestone	Team Member	Story Points
Sprint-1	Requirement Analysis & Planning	Aditya A	5
Sprint-2	Backend Development & Schema Configuration	Akash N A	11
Sprint-3	Flow Designer Automation	Radha Krishnan P	11
Sprint-4	Testing & Validation	Ferdin Joe A	5
Sprint-5	Deployment & Packaging	Simeon P	5
Total	All five milestones	Project Team	37

The 37-point total is a planning estimate mapped to the twelve documented work items. It is not presented as a historical point total from the SkillWallet board.

Project Tracker, Velocity & Burndown Chart

Sprint	Total Story Points	Duration	Sprint Start Date	Sprint End Date (Planned)	Story Points Completed	Sprint Release Date (Actual)
Sprint-1	5	1 Day	28 September 2026	28 September 2026	5	28 September 2026
Sprint-2	11	1 Day	29 September 2026	29 September 2026	11	29 September 2026
Sprint-3	11	1 Day	30 September 2026	30 September 2026	11	30 September 2026
Sprint-4	5	1 Day	01 October 2026	01 October 2026	5	01 October 2026
Sprint-5	5	1 Day	01 October 2026	01 October 2026	5	01 October 2026

The sprint dates below follow the project schedule provided for this planning document. Sprints 1 to 5 are planned as one-day work periods for this project schedule.

Velocity

Total planned story points = 37. Number of planned sprints = 5.
Average velocity = Total Story Points / Number of Sprints = 37 / 5 = **7.4 story points per sprint**.
The planning logic reference calculates team velocity as total story points divided by the number of sprints.

Burndown Chart

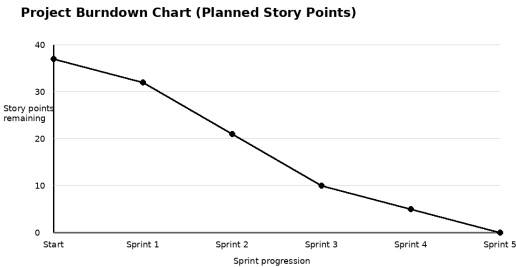


Figure 1: Planned project burndown based on the estimated 37 story points.

Burndown Chart Explanation:

The burndown chart tracks remaining story points over the course of the five sprints. The project begins with 37 estimated points at Sprint Start. Following Sprint 1 (5 points completed), 32 points remain. Sprint 2 burns down 11 points (21 remaining), Sprint 3 burns down 11 points (10 remaining), Sprint 4 burns down 5 points (5 remaining), and Sprint 5 completes the final 5 deployment points, bringing remaining effort down to 0 at release.

Implementation Evidence

The following screenshots connect the planned stories with the actual ServiceNow implementation.

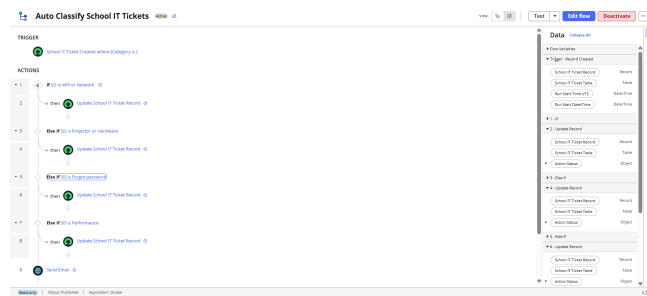


Figure 2: Published Auto Classify School IT Tickets Flow Designer workflow.

The screenshot shows the 'School IT Tickets' list view in ServiceNow. The table displays the following data:

Number	Assigned Group	Assigned To	Category	Description	Short Description	Status	Subcategory
T01000001	Service	Service	Service	Service	Service	Open	
T01000002	Service	Service	Hardware	Hardware	Hardware	Open	
T01000003	Service	Service	Network	Network	Network	Open	
T01000004	Service	Service	Performance	Performance	Performance	Open	

Figure 3: School IT Tickets list showing created records and classification results.

Implementation Evidence - Testing and Deployment

ServiceNow
School IT Ticket - 17150000000000000000

Number: 17150000000000000000
Category: Networks
Subcategory: LAN
Status: Open

Description: SIS file not working in library

Assigned To: System Administrator

Update | Delete

Figure 4: School IT Ticket showing automatic Category and Subcategory classification.

ServiceNow
Update Set: Project Update Set

Name: Project Update Set
Status: Complete
Release Date: 2020-09-28 10:11:17

Update | Back to 4

Related Links
Project Update Set
Project Update Set

Update Set	Update Set Name	Update Set Type	Update Set Status	Update Set Description
2020-09-28 10:11:17	Project Update Set	Project Update Set	Complete	Project Update Set
2020-09-28 10:11:17	Project Update Set	Project Update Set	Complete	Project Update Set
2020-09-28 10:11:17	Project Update Set	Project Update Set	Complete	Project Update Set
2020-09-28 10:11:17	Project Update Set	Project Update Set	Complete	Project Update Set
2020-09-28 10:11:17	Project Update Set	Project Update Set	Complete	Project Update Set
2020-09-28 10:11:17	Project Update Set	Project Update Set	Complete	Project Update Set
2020-09-28 10:11:17	Project Update Set	Project Update Set	Complete	Project Update Set
2020-09-28 10:11:17	Project Update Set	Project Update Set	Complete	Project Update Set
2020-09-28 10:11:17	Project Update Set	Project Update Set	Complete	Project Update Set
2020-09-28 10:11:17	Project Update Set	Project Update Set	Complete	Project Update Set

Figure 5: Completed Project Update Set with captured customer updates and the Export to XML option.
